


# Fairfield/Vacaville Train Station

Status Update  
for


Solano Transportation Authority  
June 8, 2011

Steve Hartwig  
Asst. Public Works Director / City Engineer  
City of Fairfield

# Partnership Project





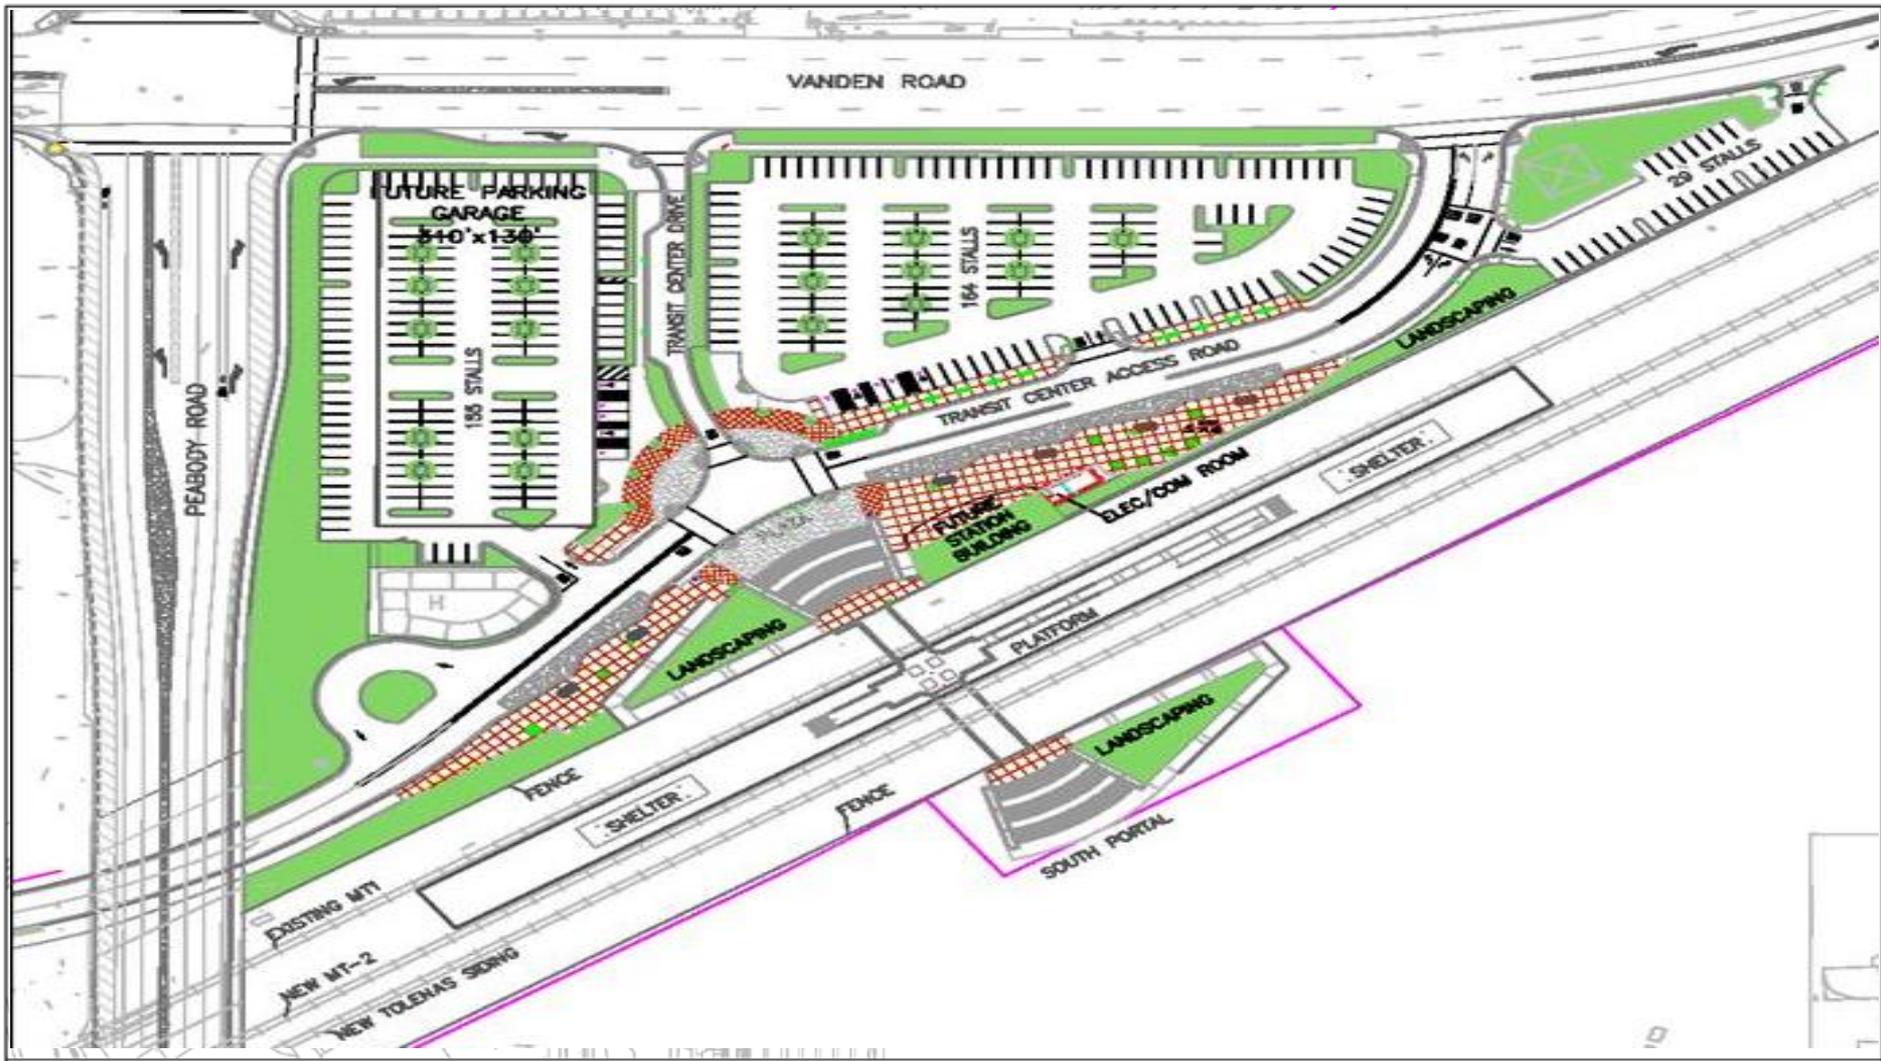

# FAIRFIELD VACAVILLE TRAIN STATION - SITE PLAN



65 % PLAN SET  
 NOV. 16, 2010  
 REVISION: 1.1



# Fairfield/Vacaville Train Station



CEMENT HILL RD.

PERBODY RD.

VANDEN RD.


Future Parking Structure

Passenger Platform

Underpass

Bus Passenger Drop Off

# Train Station Specific Plan

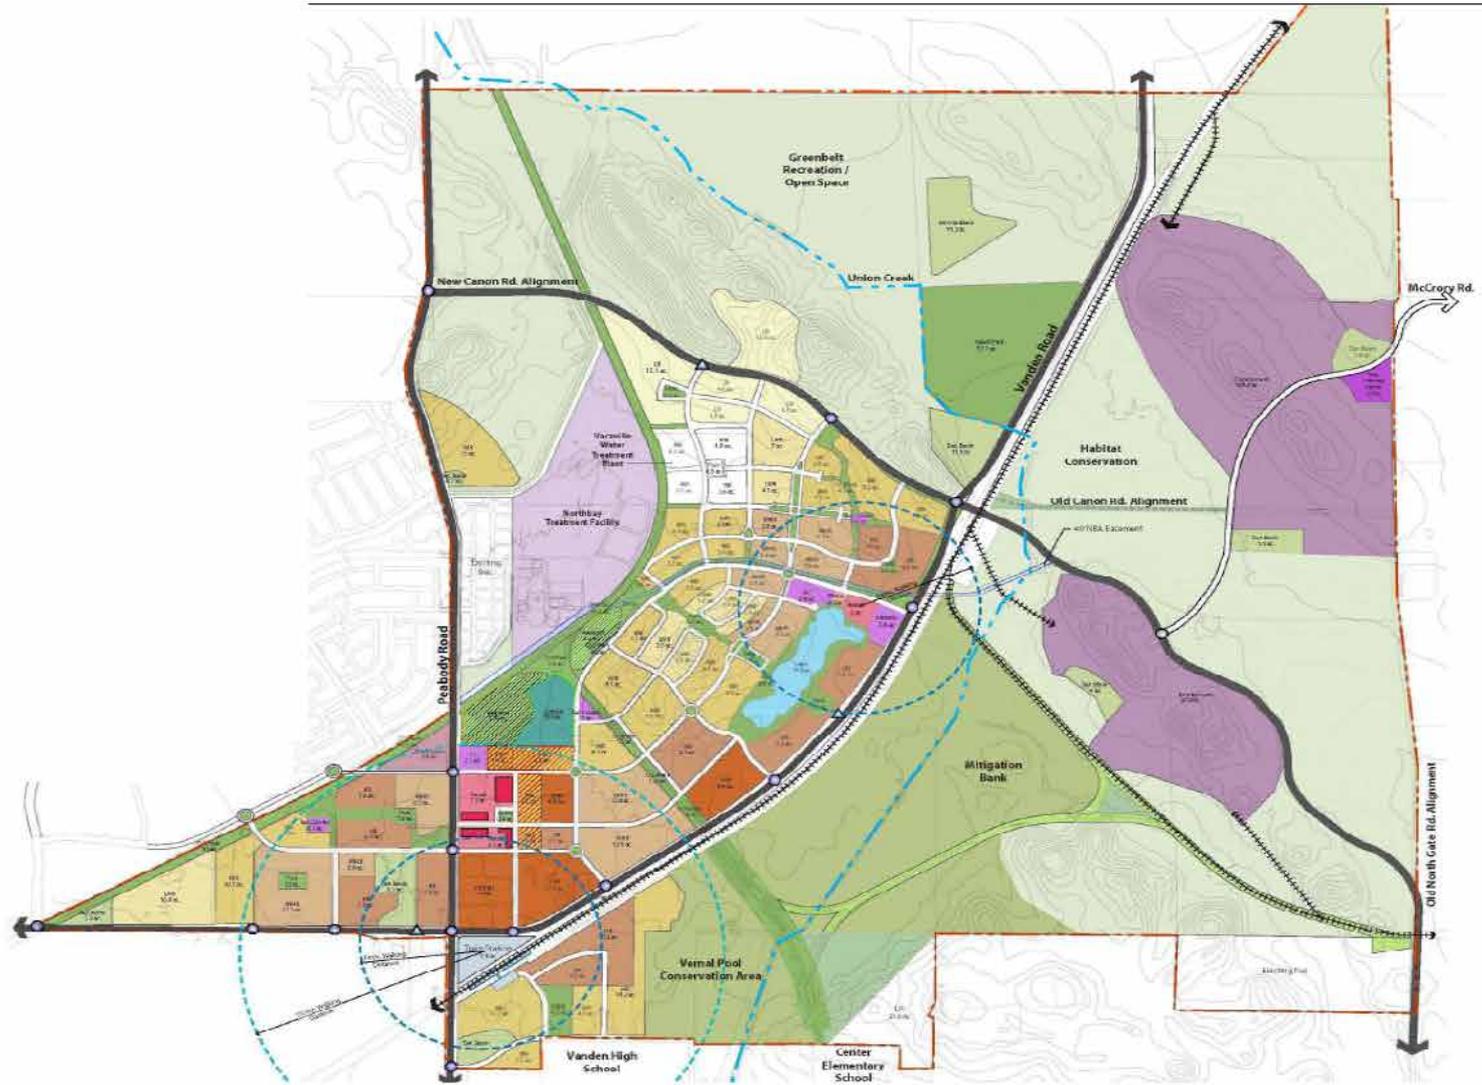



# SCHEDULE

- Project Management Contract      Dec 2008
- Design Services Contract      Oct 2009
- CEQA Complete      Jun 2010
- Begin Final Design      May 2011

---

- NEPA Complete      Sep 2011
- ROW/Design Complete      Dec 2011
- Construction Start      \*Spring 2012
- Station Open      \*Summer 2014 or 2015
- Construction Closeout      \*Fall 2014 or 2015

# Funding Plan for Station

<u>Revenue Source</u>	<u>Amount</u>	(in millions)
Regional Measure 2	\$ 27.85	
Toll Bridge	\$ 9.00	
State Grants	\$ 4.00	
Federal Grants/Earmarks	\$ 3.30	
Fairfield & Vacaville	<u>\$ 3.95</u>	
Confirmed Total	\$ 48.10	
Estimate To Complete	\$ 48	
With Bid Alternates	\$54	
- Solar Panel Array in Parking Lot		
- West Parking Facility and Vanderbilt Drive		
- South Access Portal		

Next Stop –  
Fairfield/Vacaville Intermodal Train Station

Questions?
